E.T.& L. CORP.
Stow, MA

Activity ID	Activity Name	OD	Calendar	Start	Finish	TF
Waltham - Trapelo Road Culvert (After Restriction)		225		19-Jun-24	13-May-25	-102
Milestones		329	7 Day	19-Jun-24	13-May-25	-149
0	Start Field Construction	0	7 Day	19-Jun-24*		-141
45	Final Completion	0	7 Day		13-May-25	-149
Preliminary Stage		15		19-Jun-24	10-Jul-24	-98
1	Install Stakes and Flags Marking Wetland and Limits of work	1	5 Day	19-Jun-24	19-Jun-24	-98
2	Pre-Construction Walk With Conservation Commissions	1	5 Day	20-Jun-24	20-Jun-24	-98
3	Notify Conservation Commissions 48 Hours Prior to Commencement of Work	1	5 Day	21-Jun-24	21-Jun-24	-98
4	Clearing and Grubbing	2	5 Day	24-Jun-24	25-Jun-24	-98
5	Install Erosion Control	1	5 Day	26-Jun-24	26-Jun-24	-98
6	Notifiy Conservation Commissions Upon Completion of Erosion Control Installatio	1	5 Day	27-Jun-24	27-Jun-24	-98
7	Conservation Commissions Inspect and Approve Erosion Control (Potential Meet	1	5 Day	28-Jun-24	28-Jun-24	-98
8	Install Trench Box Excavate and Install Temporary 42"ADS PIpe (100 LF) using L	4	5 Day (River Herring Restriction)	01-Jul-24	05-Jul-24	-35
9	Reconnect Catch Basin to 42" Diversion Pipe	1	5 Day (River Herring Restriction)	08-Jul-24	08-Jul-24	-35
10	Connect Existing 18" VC to Diversion Pipe	1	5 Day (River Herring Restriction)	09-Jul-24	09-Jul-24	-35
11	Backfill and Pave over Diversion Pipe Excavation	1	5 Day (River Herring Restriction)	10-Jul-24	10-Jul-24	-35
Stage 1A		21	5 Day (River Herring Restriction)	11-Jul-24	08-Aug-24	-35
12	Implement Traffic Detour Install Barriers as Shown on Staging Plan - Stage 1 Rer	1	5 Day (River Herring Restriction)	11-Jul-24	11-Jul-24	-35
13	Install Sandbags and Redirect Stream Flow Through Diversion Pipe	3	5 Day (River Herring Restriction)	12-Jul-24	16-Jul-24	-35
14	Demolish Downstream Wall	2	5 Day (River Herring Restriction)	17-Jul-24	18-Jul-24	-35
15	Construct Wingwalls and Proposed Drainage System as Shown and Plug 15" RC	5	5 Day (River Herring Restriction)	19-Jul-24	25-Jul-24	-35
16	Install Temporary Support of Excavation	2	5 Day (River Herring Restriction)	26-Jul-24	29-Jul-24	-35
17	Demolish South Half of Culvert	8	5 Day (River Herring Restriction)	30-Jul-24	08-Aug-24	-35
Stage 1B		69		01-Jul-24	07-Oct-24	-35
F&D 1	Fabricate and Deliver Box Culvert	1	5 Day (River Herring Restriction)	01-Jul-24	01-Jul-24	-8
18	Construct South Half of Culvert and Wingwalls	21	Winter (River Herring Restriction)	09-Aug-24	09-Sep-24	-35
19	Construct Block Wall Moment Slab and Bridge Raling	11	5 Day (River Herring Restriction)	10-Sep-24	24-Sep-24	-35
20	Construct CB and 12" DI Pipe and Remove EX CB as Shown	3	5 Day (River Herring Restriction)	25-Sep-24	27-Sep-24	-35
21	Construct Sidewalk and Curbing	2	Winter (River Herring Restriction)	30-Sep-24	01-Oct-24	-35
22	Gravel and Dense Grade Fine Grade	3	5 Day (River Herring Restriction)	02-Oct-24	04-Oct-24	-35
23	Install Base and Intermediate Course - East Half	1	Paving (River Herring Restriction)	07-Oct-24	07-Oct-24	-35
Stage 2		148		08-Oct-24	13-May-25	-102
24	Install Barrier as Shown on Staging Plan - Stage 2 and Shift Traffic Southbound	1	5 Day (River Herring Restriction)	08-Oct-24	08-Oct-24	-35
25	Demolish North Half of Culvert and Upstream Headwall	8	5 Day (River Herring Restriction)	09-Oct-24	21-Oct-24	-35
26	Construct North Half of Culvert and Wingwalls	24	Winter (River Herring Restriction)	22-Oct-24	25-Nov-24	-35
27	Remove Temporary Support of Excavation	1	5 Day (River Herring Restriction)	26-Nov-24	26-Nov-24	-35
28	Install Flood Wall	19	Winter	26-Nov-24	07-Apr-25	-16
29	Shift Stream Flow Through New Culvert	1	5 Day (River Herring Restriction)	17-Mar-25*	17-Mar-25	-108
30	Remove Projecting Ends of 42"ADS Pipe and Flowfill Remainder	3	5 Day (River Herring Restriction)	18-Mar-25	20-Mar-25	-108
31	Install Remaining Catch Basin Manhole and Pipe	3	5 Day	21-Mar-25	25-Mar-25	-108
32	Install Guardrail Transitions	1	5 Day	26-Mar-25	26-Mar-25	-108
33	Coordinate Gas Main Replacement	1	5 Day	27-Mar-25	27-Mar-25	-108
34	Install Gravel Borrow Dense Grade and Fine Grade	3	5 Day	28-Mar-25	01-Apr-25	-108
35	Install Base and Intermediate Course - North Half	1	Paving	30-Apr-25*	30-Apr-25	-134
36	Install Top Course	1	Paving	01-May-25	01-May-25	-134
37	Install Pavement Markings	1	5 Day	02-May-25	02-May-25	-127
38	Install Loam	1	5 Day	05-May-25	05-May-25	-127
39	Seed	1	Seeding	06-May-25	06-May-25	-25
40	Install Plantings	1	Deciduous Plantings	07-May-25	07-May-25	-33
41	Remove Erosion Control Measures	1	5 Day	08-May-25	08-May-25	-102
42	Submit Request for Certificate of Compliance to Conservation Commissions	1	5 Day	09-May-25	09-May-25	-102
43	Conservation Commissions Approve Request for Certificate of Compliance	1	5 Day	12-May-25	12-May-25	-102
44	Remove Traffic Control	1	5 Day	13-May-25	13-May-25	-102

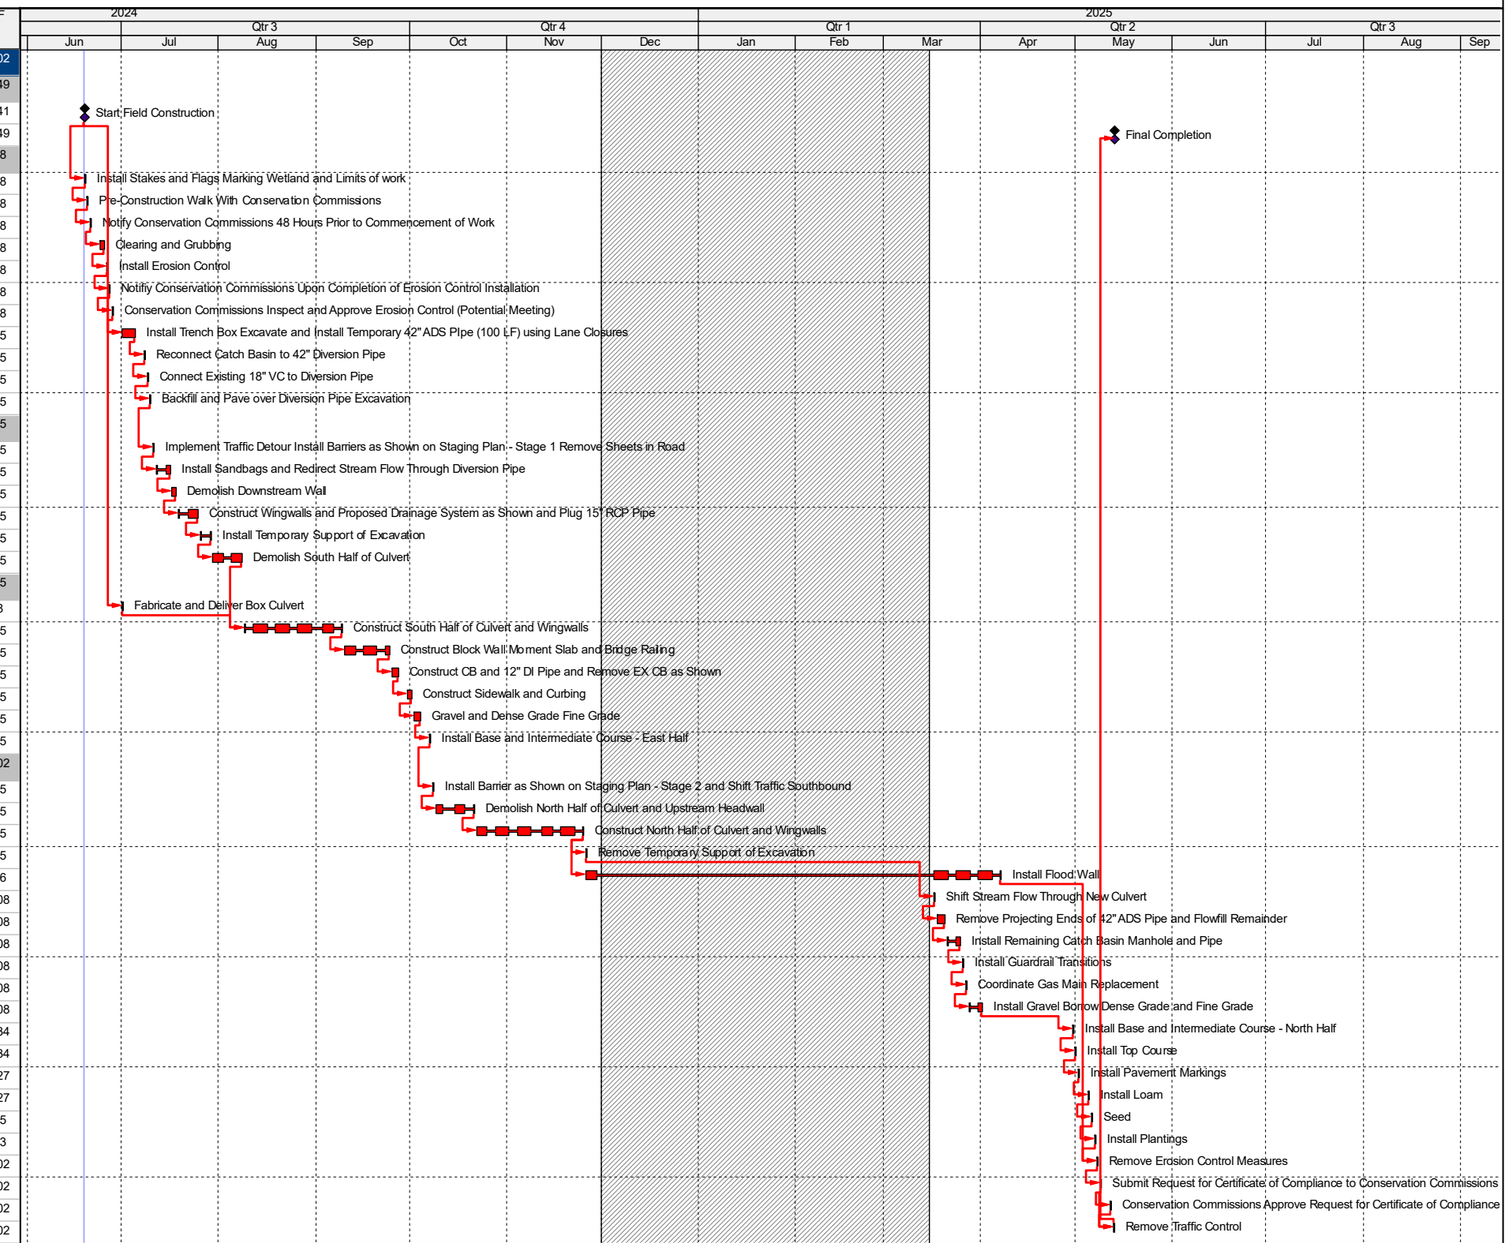

Actual Work
Remaining Work
Critical Remaining Work
Prim BL Milestones
Milestone

Waltham - Trapelo Road Culvert (After Restriction)
Baseline Schedule - All Activities

Data Date = 19-Jun-24 Run Date = 15-Aug-23, 09:49
Project Start = 19-Jun-24 Project Finish = 13-May-25

Date	Revision	Checked	Approved

User: Brad

TASK filter: All Activities
